



# MEBT MEETING AGENDA

September 27, 2001

---

## Mechanical Systems Update

### 1. Raft Assembly Status

- Rebuncher installed on Raft 3 ([photo](#))
- BPM shimming ([photo](#))
- Rafts 1 & 2 ([photo](#))

### 2. Fabrication and Procurement Update

- Raft weldments COMPLETED 0
- Profile Monitor Beambox welding COMPLETED 0
- Beampipe 1&2 repair underway
- Other fabrications underway:
  - raft assembly tooling
  - raft water manifolds

### 3. Design Status ([MEBT](#))

- Raft assembly drawings
- Water system
- Quad power lead routing
- Quad Electrical Covers

## Electrical Systems Update

### 1. Low Level RF

### 2. Rebuncher System

### 3. Beam Diagnostics

## System Integration / Installation


### 1. Installation of MEBT frame

## Upcoming Tasks and Milestones

- ◆ Rafts and Support Structure COMPLETED 0 9/14/01 OR
- ◆ Rebuncher Cavity #2-4 Received 6/30/01
- ◆ Profile Monitor all complete 7/31/01
- ◆ MEBT Raft 3 assembly complete 9/30/01

*Next Meeting: Thursday, 10/11/01, 10 AM*



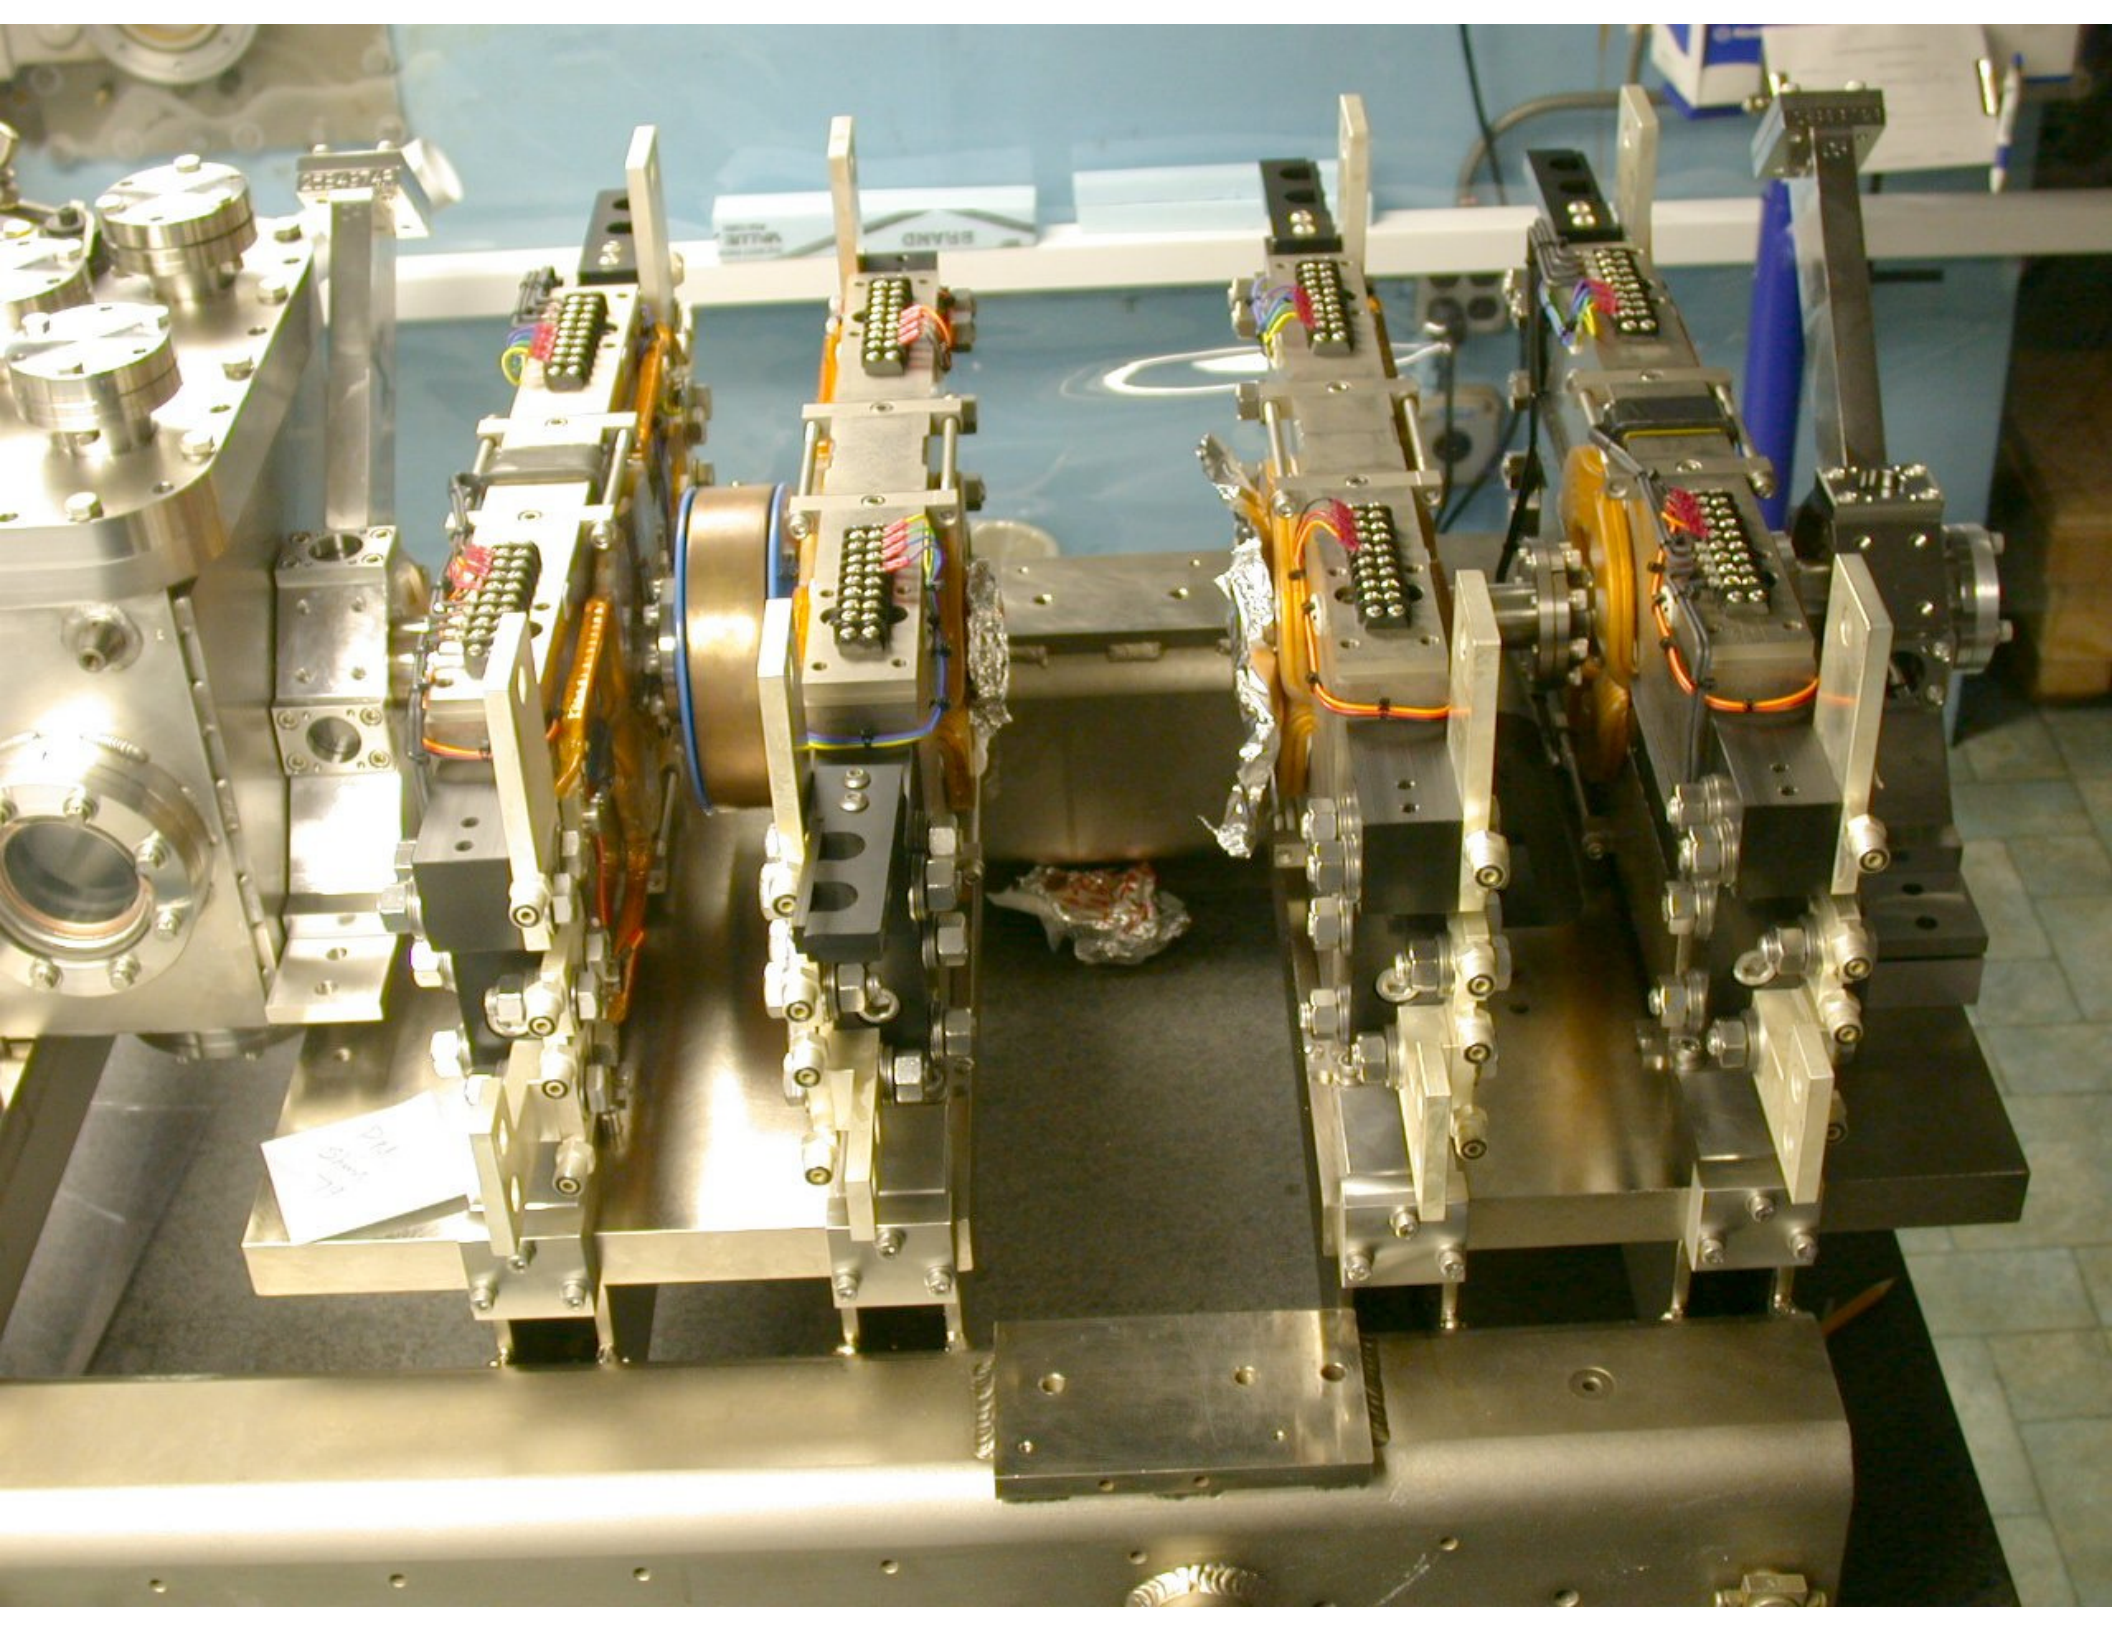

D11  
Stand  
71

BRAND  
WITTE

